

Access for All

Wales and Borders - May 2024

Hello and welcome to the latest edition of our monthly newsletter that showcases our work to improve accessibility across the Wales and Borders route.

Work has continued across 6 stations this last month, with many milestones achieved. This month is no different as we get closer to completion.

We have detailed the latest from each of the Access for All stations below, and hope that you find these updates useful.



Llanelli Station, April 2024

- Flint -

We are ready to begin piling works at Flint from 7 May 2024.

Until our work is completed, passengers will need to continue to use the alternative footbridge at the end of the platform until the new footbridge and lifts have been completed.

Cwmbran

We have successfully completed piling and groundwork at Cwmbran, with the most recent work being installing the lift shafts. The stairs and main span are planned to be added throughout May.

In the image on the right, you can see one of the lift shafts being lowered into place.



Access for All - Wales and Borders

.lanelli

Over the last weekend, the main span was lowered into place and the bridge is starting to take shape.

Over the next few weeks, work will begin to install the lift shafts.

Work will continue to take place over Saturday night shifts throughout May.

Ludlow

The frame for the lift has been installed and the masonry cladding is continuing.

We've also completed a substantial amount of ducting along the platforms.



Abergavenny



After discovering redundant pipework at platform 2, (*pictured left*) we have now completed all the ducting work and diverted the necessary cables for us to continue at Abergavenny.

We can now begin piling works from 7 May.

We have constructed an access road off the A465 so that we can transport materials to site without impacting the local community.

Got a Question?

There are several ways to reach us. You can call our 24-hour dedicated helpline on **03457114141**; emailing us at **CRWales@networkrail.co.uk** or visit our website: https://www.networkrail.co.uk/AFAWalesandborders

Working in partnership with:

Department for Transport

TRAFNIDIAETH CYMRU TRANSPORT FOR WALES Gwasanaethau Rheilffyrdd Rail Services

Newtown

There's continued works to platform ducting at Newtown, with platform 1 being substantially completed.

Work will continue on Saturday night shifts throughout May where columns and lift shafts are expected to be completed.

Pictured is some of the foundations work that has






Mynediad i Bawb

Cymru a'r Gororau – Mai 2024

Helo a chroeso i rifyn diweddaraf ein cylchlythyr misol yn dangos ein gwaith i wella hygyrchedd ar draws llwybr Cymru a'r Gororau.

Mae'r gwaith wedi parhau i fynd rhagddo mewn chwe gorsaf fis diwethaf, gan gyrraedd sawl carreg filltir. Nid yw'r mis hwn yn wahanol wrth inni nesáu at gwblhau'r gwaith.

Mae'r newyddion diweddaraf am y gwaith ym mhob gorsaf Mynediad i Bawb isod. Gobeithio y bydd y diweddariadau hyn yn o ddefnydd ichi.

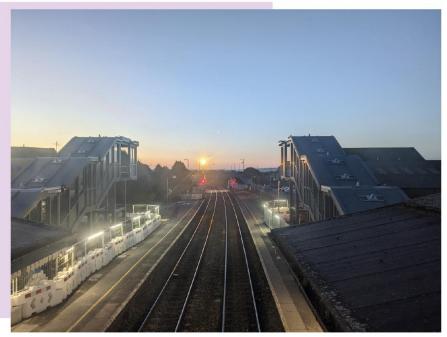

Gorsaf Llanelli, Ebrill 2024

-Y Fflint

Rydym yn barod i ddechrau ar y gwaith stancio yn y Fflint ar 7 Mai 2024.

Hyd at ddiwedd ein gwaith i osod y bont droed newydd a'r lifftiau yn eu lle, rhaid i deithwyr barhau i ddefnyddio'r bont droed amgen ar ddiwedd y platfform.

Cwmbrân

Rydym wedi cwblhau'r gwaith stancio a gwaith paratoi'r pridd yng Nghwmbrân yn llwyddiannus. Gosod siafftiau'r lifftiau oedd y gwaith mwyaf diweddar. Byddwn yn ychwanegu'r grisiau a'r prif fwa yn ystod mis Mai.

Mae'r llun ar y dde yn dangos un o'r siafftiau lifft yn cael ei osod yn ei le.



Mai 2024

lane

Gosodwyd prif fwa'r bont yn ei le penwythnos diwethaf, ac mae'r bont yn dechrau dod at ei gilydd.

Bydd y gwaith i osod siafftiau'r lifftiau yn dechrau'n ystod yr wythnosau nesaf.

Bydd y gwaith yn parhau i fynd rhagddo yn ystod shifftiau nos Sadwrn drwy gydol mis Mai.



Llwydlo -

Cafodd ffrâm y lifft ei osod yn ei le ac mae'r gwaith i roi cladin cerrig arni yn parhau.

Rydym hefyd wedi gwneud gwaith sylweddol yn gosod dwythellau ar hyd y platfformau.



Y Fenni

Y Drenewydd Mae'r gwaith yn parhau i fynd

rhagddo yn gosod dwythellau'r platfformau yn y Drenewydd, ac mae'r awaith ar blatfform 1 wedi'i gwblhau i raddau helaeth.

Bydd y gwaith yn parhau yn ystod shifftiau nos Sadwrn drwy gydol mis Mai, a disgwylir i'r gwaith o osod colofnau a siafftiau'r lifft gael ei gwblhau'r pryd hwnnw.

Mae'r llun yn dangos rhywfaint o'r gwaith a gwblhawyd ar y sylfeini hyd yma.





Ar ôl dod o hyd i bibellau segur ar blatfform 2, rydym bellach wedi cwblhau'r holl waith i osod dwythellau ac wedi ailgyfeirio'r ceblau sydd eu hangen arnom i barhau â'n gwaith yn y Fenni.

Gallwn ddechrau ar y gwaith stancio ar 7 Mai.

Rydym wedi adeiladu ffordd mynediad oddi ar ffordd yr A465 er mwyn inni aludo deunyddiau i'r safle heb effeithio ar y gymuned leol.

Unrhyw gwestiynau?

Mae sawl ffordd o gysylltu â ni. Gallwch ffonio ein llinell gymorth 24-awr ar 03457114141; anfon e-bost at CRWales@networkrail.co.uk neu fynd i'n gwefan: https://www.networkrail.co.uk/AFAWalesandborders

Gweithio mewn partneriaeth â:

Xō. Department for Transport

TRAFNIDIAETH CYMRU TRANSPORT FOR WALES Gwasanaethau Rheilffyrdd **Rail Services**
